| ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|
| 1 | *MoDot Project: JNW0049* | *29 days* | *Mon 5/4* | *Thu 6/11* |
| 2 | Install Post Mounted Signs | 3 days | Mon 4/20 | Wed 4/22 |
| 3 | ESS CONSTRUCTION SCHEDULE: | 23 days | Mon 5/4 | Wed 6/3 |
| 4 | 0.5" Scratch Course (9,785.75 tons): | 7 days | Mon 5/4 | Tue 5/12 |
| 5 | 0.5" Scratch Course Paving (WBL from LM 18.60 to LM 32.893) - From 4-way to end of project | 2.75 days | Mon 5/4 | Wed 5/6 |
| 6 | 0.5" Scratch Course Paving (EBL from LM 32.893 to LM 18.60)- From end of project to 4-way | 2.75 days | Thu 5/7 | Mon 5/11 |
| 7 | 0.5" Scratch Course Paving (both lanes LM 18.273 to LM 18.60) | 0.5 days | Tue 5/12 | Tue 5/12 |
| 8 | Coldmilling (Depth Transitions LM 18.60 - 32.839) 4-way to end of Project | 1 day | Mon 5/11 | Mon 5/11 |
| 9 | Coldmilling (Depth Transitions & Curb Cuts LM 18.236 - 18.60) Start of Project to 4-way | 0.5 days | Mon 5/11 | Mon 5/11 |
| 10 | 1" Surface Level Overlay (13,047.55 tons): | 8 days | Tue 5/12 | Thu 5/21 |
| 11 | 1" Surface Level Paving (LM 18.236 to LM 27.75) Start of project to Route Z - Matching Daily | 3.25 days | Tue 5/12 | Fri 5/15 |
| 12 | 1" Surface Level Paving (LM27.75 to LM 32.893 to LM 27.75) From route Z to end of project & back - Racetrack | 2.75 days | Fri 5/15 | Wed 5/20 |
| 13 | 1" Surface Level Paving - Remaining Driveways / Entrances / Side roads (Harrisonville) | 0.5 days | Thu 5/21 | Thu 5/21 |
| 14 | Edge Treatment (7,497 tons): | 6 days | Mon 5/25 | Mon 6/1 |
| 15 | Agg Edge Rock (Type 5) | 6 days | Mon 5/25 | Mon 6/1 |
| 16 | SUBCONTRACTORS: | 7 days | Wed 6/3 | Thu 6/11 |
| 17 | Dripline | 1 day | Wed 6/3 | Wed 6/3 |
| 18 | Rumble Strips | 2 days | Fri 6/5 | Mon 6/8 |
| 19 | Pavement Markings | 2 days | Wed 6/10 | Thu 6/11 |

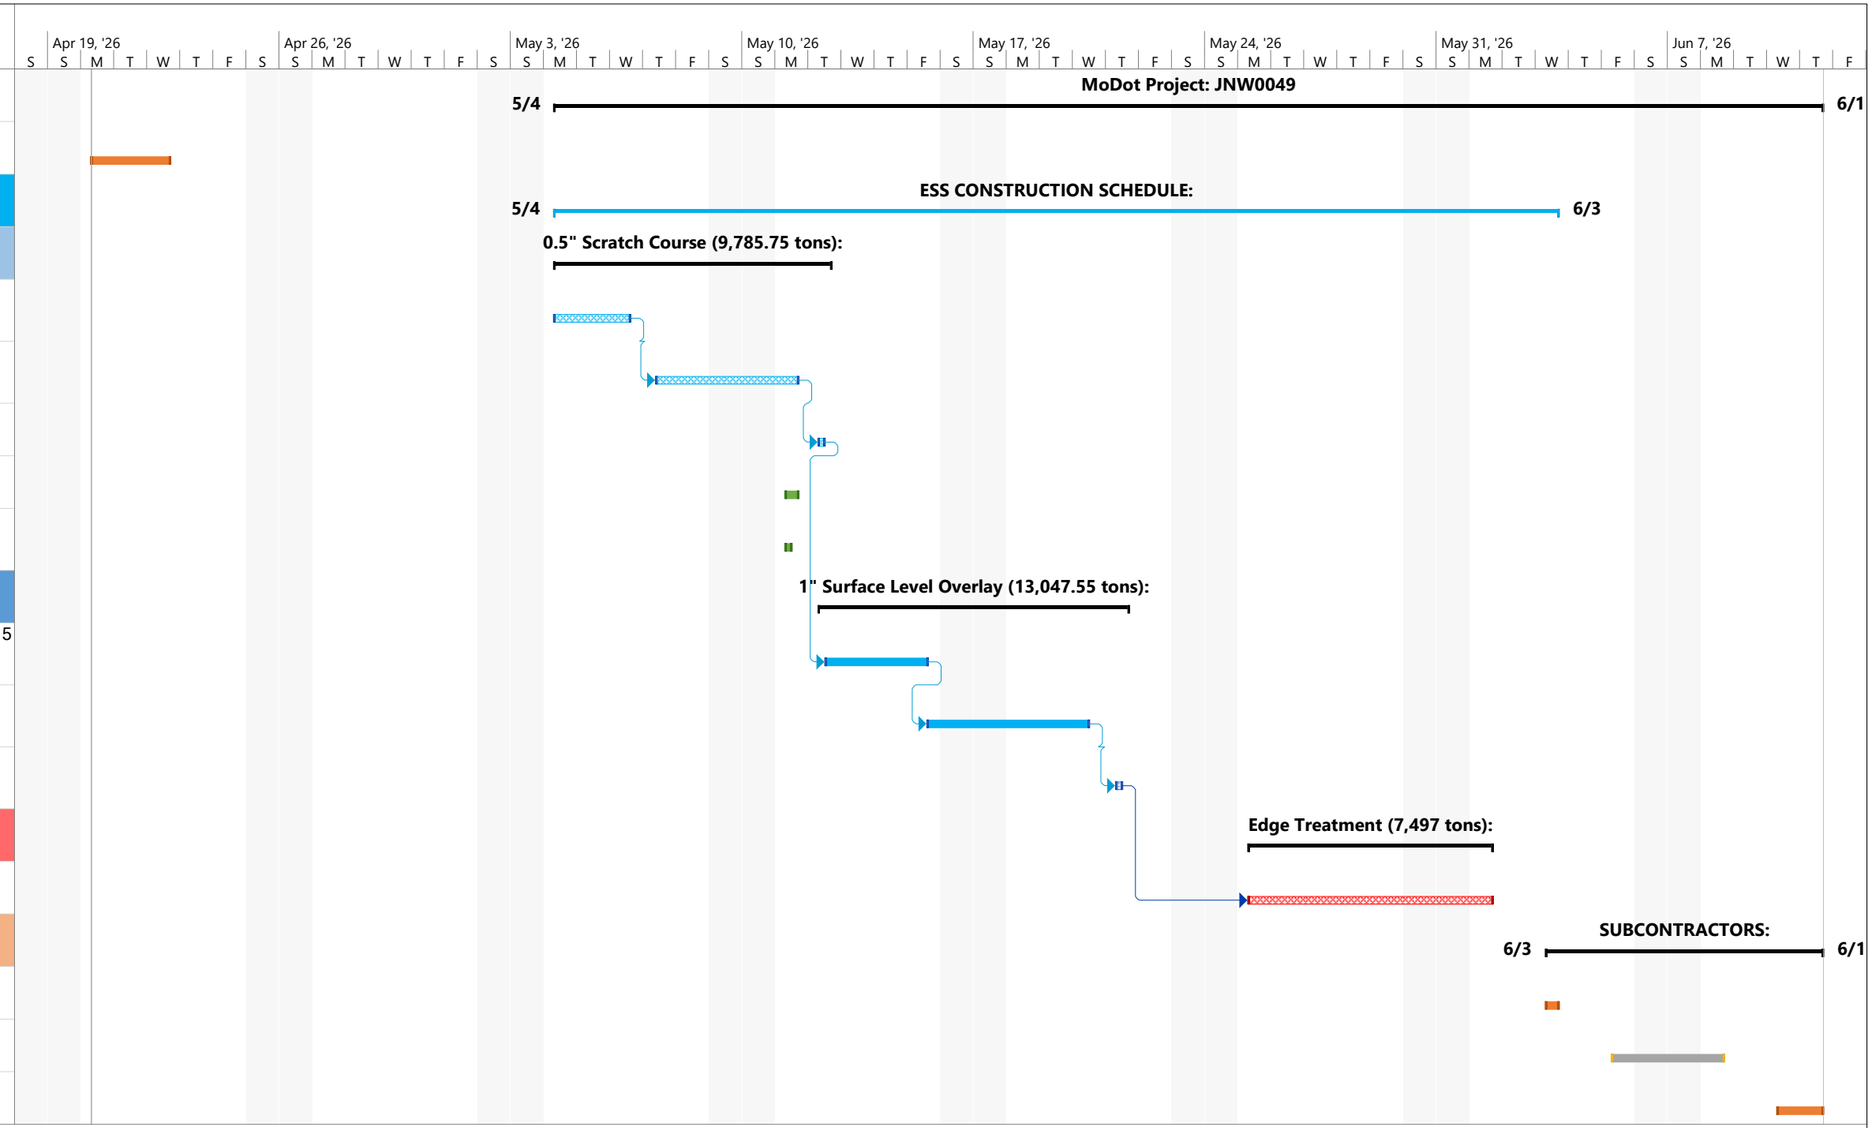


Project: Route 2 (1625132) - Pr
Date: Tue 4/14

| | | | | |
|---|---|---|---|---|
| Task | Project Summary | Manual Task | Start-only | Deadline |
| Split | Inactive Task | Duration-only | Finish-only | Progress |
| Milestone | Inactive Milestone | Manual Summary Rollup | External Tasks | Manual Progress |
| Summary | Inactive Summary | Manual Summary | External Milestone | |
